











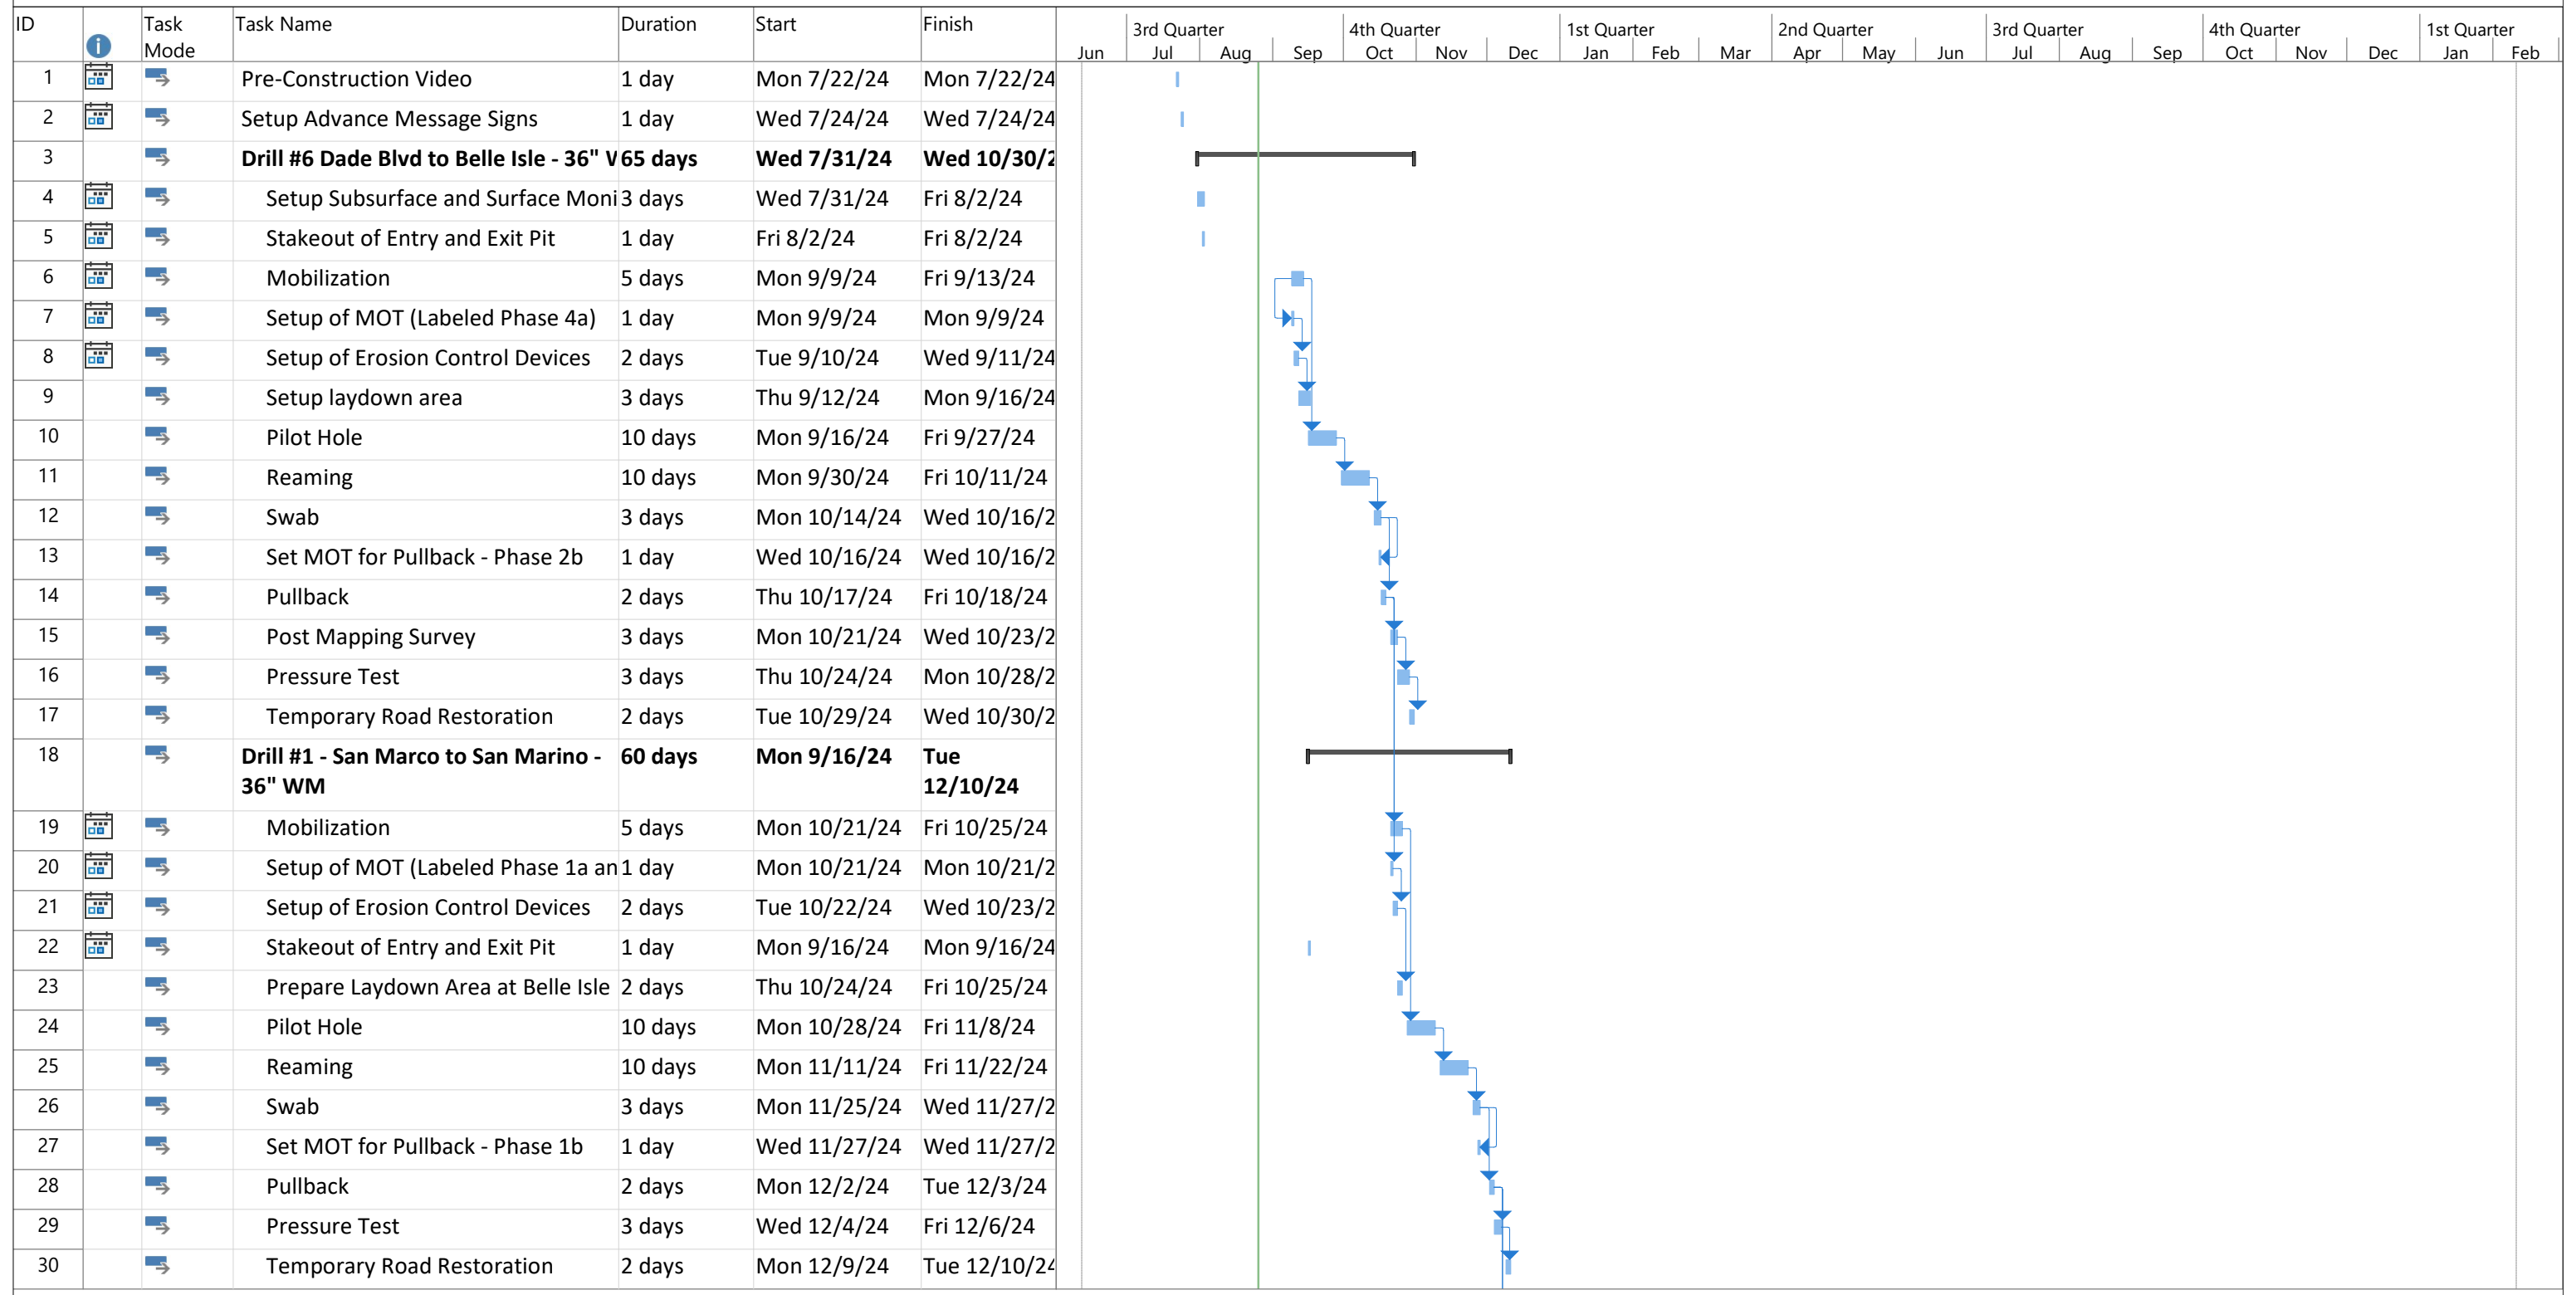









Venetian Causeway Phase 2 - Schedule



Project: Venetian Causeway Pha
Date: Mon 8/26/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Venetian Causeway Phase 2 - Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	Timeline																							
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb			
31		Drill #2 Di Lido to San Marino - 36" W	61 days	Mon 10/28/24	Tue 1/28/25																								
32		Mobilization	5 days	Wed 12/4/24	Tue 12/10/24																								
33		Setup of MOT (Labeled Phase 2a an	1 day	Wed 12/4/24	Wed 12/4/24																								
34		Setup of Erosion Control Devices	2 days	Thu 12/5/24	Fri 12/6/24																								
35		Stakeout of Entry and Exit Pit	1 day	Mon 10/28/24	Mon 10/28/24																								
36		Pilot Hole	10 days	Wed 12/11/24	Thu 12/26/24																								
37		Reaming	10 days	Fri 12/27/24	Mon 1/13/25																								
38		Swab	3 days	Tue 1/14/25	Thu 1/16/25																								
39		Set MOT for Pullback - Phase 2b	1 day	Thu 1/16/25	Thu 1/16/25																								
40		Pullback	2 days	Fri 1/17/25	Mon 1/20/25																								
41		Post Mapping Survey	3 days	Tue 1/21/25	Thu 1/23/25																								
42		Pressure Test	3 days	Fri 1/24/25	Tue 1/28/25																								
43		Drill #3 Di Lido to San Marino - 12" F	20 days	Fri 1/24/25	Thu 2/20/25																								
44		Setup of MOT (Labeled Phase 2a an	1 day	Fri 1/24/25	Fri 1/24/25																								
45		Pilot Hole	5 days	Fri 1/24/25	Thu 1/30/25																								
46		Reaming	6 days	Fri 1/31/25	Fri 2/7/25																								
47		Swab	2 days	Mon 2/10/25	Tue 2/11/25																								
48		Set MOT for Pullback - Phase 2b	1 day	Tue 2/11/25	Tue 2/11/25																								
49		Pullback	2 days	Wed 2/12/25	Thu 2/13/25																								
50		Pressure Test	3 days	Fri 2/14/25	Tue 2/18/25																								
51		Temporary Road Restoration on Sa	2 days	Wed 2/19/25	Thu 2/20/25																								
52		Drill #4 Di Lido to Rivo Alto - 36" WM	61 days	Fri 1/10/25	Fri 4/4/25																								
53		Reset of Drill Rig	5 days	Fri 2/14/25	Thu 2/20/25																								
54		Setup of MOT (Labeled Phase 3a an	1 day	Fri 2/14/25	Fri 2/14/25																								
55		Setup of Erosion Control Devices	2 days	Mon 2/17/25	Tue 2/18/25																								
56		Stakeout of Entry and Exit Pit	1 day	Fri 1/10/25	Fri 1/10/25																								
57		Pilot Hole	10 days	Fri 2/21/25	Thu 3/6/25																								
58		Reaming	10 days	Fri 3/7/25	Thu 3/20/25																								
59		Swab	3 days	Fri 3/21/25	Tue 3/25/25																								
60		Set MOT for Pullback - Phase 2b	1 day	Tue 3/25/25	Tue 3/25/25																								
61		Pullback	2 days	Wed 3/26/25	Thu 3/27/25																								

Project: Venetian Causeway Pha Date: Mon 8/26/24	Task Project Summary Split Inactive Task Milestone Inactive Milestone Summary Inactive Summary	Manual Task Manual Task Duration-only Duration-only Manual Summary Rollup Manual Summary Rollup Manual Summary Manual Summary	Start-only Start-only Finish-only Finish-only External Tasks External Tasks External Milestone External Milestone	Deadline Deadline Progress Progress Manual Progress Manual Progress
---	---	--	--	--

Venetian Causeway Phase 2 - Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	3rd Quarter		4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter	
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
62	→	Post Mapping Survey	3 days	Fri 3/28/25	Tue 4/1/25																			
63	→	Pressure Test	3 days	Wed 4/2/25	Fri 4/4/25																			
64	→	Drill #5 Di Lido to Rivo Alto - 12" FM	22 days	Wed 4/2/25	Thu 5/1/25																			
65	→	Setup of MOT (Labeled Phase 2a an	1 day	Wed 4/2/25	Wed 4/2/25																			
66	→	Pilot Hole	5 days	Wed 4/2/25	Tue 4/8/25																			
67	→	Reaming	6 days	Wed 4/9/25	Wed 4/16/25																			
68	→	Swab	2 days	Thu 4/17/25	Fri 4/18/25																			
69	→	Set MOT for Pullback - Phase 2b	1 day	Fri 4/18/25	Fri 4/18/25																			
70	→	Pullback	2 days	Mon 4/21/25	Tue 4/22/25																			
71	→	Pressure Test	3 days	Wed 4/23/25	Fri 4/25/25																			
72	→	Temporary Road Restoration on Di	4 days	Mon 4/28/25	Thu 5/1/25																			
73	→	San Marco - WM DIP Installation	23 days	Fri 5/2/25	Wed 6/4/25																			
74	→	Setup MOT per Phase 1a	1 day	Fri 5/2/25	Fri 5/2/25																			
75	→	Stakeout of open cut (all areas)	1 day	Fri 5/2/25	Fri 5/2/25																			
76	→	Delivery of Materials	2 days	Mon 5/5/25	Tue 5/6/25																			
77	→	Installation of 30 and 36" DIP Pipe	8 days	Wed 5/7/25	Fri 5/16/25																			
78	→	Installation fo ARV	2 days	Mon 5/19/25	Tue 5/20/25																			
79	→	Exfiltration trench repair	10 days	Wed 5/21/25	Wed 6/4/25																			
80	→	San Marino - WM and FM DIP Installa	26 days	Thu 6/5/25	Fri 7/11/25																			
81	→	Setup MOT per Phase 2a	1 day	Thu 6/5/25	Thu 6/5/25																			
82	→	Installation of 8 through 36" WM D	8 days	Fri 6/6/25	Tue 6/17/25																			
83	→	Installation fo ARV	2 days	Wed 6/18/25	Thu 6/19/25																			
84	→	Installation of 4 - 12" FM DIP Pipe	8 days	Fri 6/20/25	Tue 7/1/25																			
85	→	Exfiltration Trench Repair	5 days	Wed 7/2/25	Wed 7/9/25																			
86	→	Temporary Restoration	2 days	Thu 7/10/25	Fri 7/11/25																			
87	→	Di Lido - WM and FM DIP Installation	23 days	Mon 7/14/25	Wed 8/13/25																			
88	→	Setup MOT per Phase 3a	1 day	Mon 7/14/25	Mon 7/14/25																			
89	→	Installation of 8 through 36" WM D	8 days	Tue 7/15/25	Thu 7/24/25																			
90	→	Installation fo ARV	2 days	Fri 7/25/25	Mon 7/28/25																			
91	→	Installation of 8 - 12" FM DIP Pipe	5 days	Tue 7/29/25	Mon 8/4/25																			
92	→	Exfiltration Trench Repair	5 days	Tue 8/5/25	Mon 8/11/25																			


Project: Venetian Causeway Pha

Date: Mon 8/26/24

Task		Project Summary		Inactive Task		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		External Tasks		Manual Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Milestone		Manual Progress			
Summary		Inactive Summary		Manual Summary		External Milestone					

Venetian Causeway Phase 2 - Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter	
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
93	→	Temporary Restoration	2 days	Tue 8/12/25	Wed 8/13/25																				
94	→	Rivo Alto - WM and FM DIP Installati	22 days	Thu 8/14/25	Mon 9/15/25																				
95	→	Installation of 16 through 36" WM DIP Pipe	8 days	Thu 8/14/25	Mon 8/25/25																				
96	→	Installation fo ARV	2 days	Tue 8/26/25	Wed 8/27/25																				
97	→	Installation of 12" FM DIP Pipe	5 days	Thu 8/28/25	Thu 9/4/25																				
98	→	Exfiltration Trench Repair	5 days	Fri 9/5/25	Thu 9/11/25																				
99	→	Temporary Restoration	2 days	Fri 9/12/25	Mon 9/15/25																				
100	→	Belle Isle and Dade Blvd - WM DIP Installation	12 days	Tue 9/16/25	Wed 10/1/25																				
101	→	Installation of 20 through 36" WM DIP Pipe	10 days	Tue 9/16/25	Mon 9/29/25																				
102	→	Installation fo ARV	2 days	Tue 9/30/25	Wed 10/1/25																				
103	→	Pressure Test of WM Line	10 days	Thu 10/2/25	Wed 10/15/25																				
104	→	Chlorination of WM Line (Including wait time for DEP Clearance)	15 days	Thu 10/16/25	Wed 11/5/25																				
105	→	Pressure Test FM Line	5 days	Thu 10/30/25	Wed 11/5/25																				
106	→	Connection of FM Line	2 days	Thu 11/6/25	Fri 11/7/25																				
107	→	Connection of WM Line	2 days	Mon 11/10/25	Tue 11/11/25																				
108	→	Pipe abandonment	20 days	Wed 11/12/25	Thu 12/11/25																				
109	→	Concrete Work (Curb and Gutter, Sidewalk, etc)	5 days	Fri 12/12/25	Thu 12/18/25																				
110	→	Milling and Resurfacing	5 days	Fri 12/19/25	Tue 12/30/25																				
111	→	Temporary Striping	2 days	Mon 1/5/26	Tue 1/6/26																				
112	→	Permanent Striping	2 days	Fri 1/23/26	Mon 1/26/26																				
113	→	Post Construction Video	1 day	Tue 1/27/26	Tue 1/27/26																				
114	→	Punch List	20 days	Wed 1/7/26	Tue 2/3/26																				
115	→	Closeout Documents	25 days	Wed 1/7/26	Tue 2/10/26																				

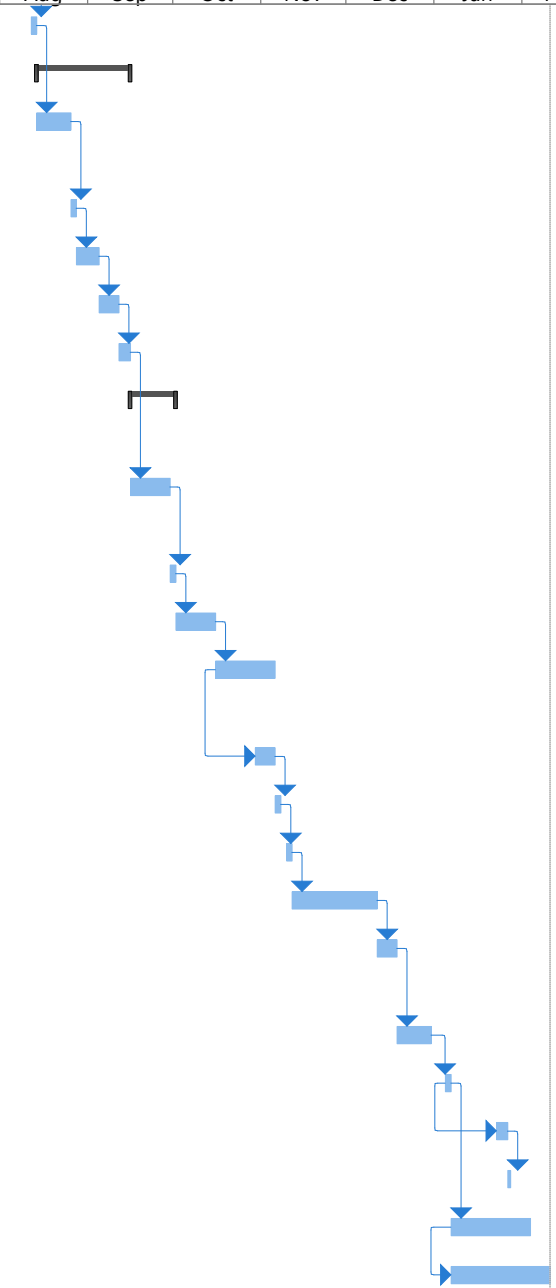

Project: Venetian Causeway Phase 2 Date: Mon 8/26/24	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
